





Location and Design Report

P.I. 0007164

CONCUR: *Mike Bonin*  
GDOT Director of Engineering

APPROVE: *Bill R. M'M* *2/20/14*  
GDOT Chief Engineer Date


DATE OF LOCATION AND DESIGN APPROVAL: *February 25, 2014*  
(To be entered by State Conceptual Design Group Manager)

Attachments:

- Sketch Map
- Notice of Location and Design Approval
- Preconstruction Status Report

Project Number: CSBRG-0007-00(164)  
PI Number: 0007164  
County: Coffee

State of Georgia  
Department of Transportation

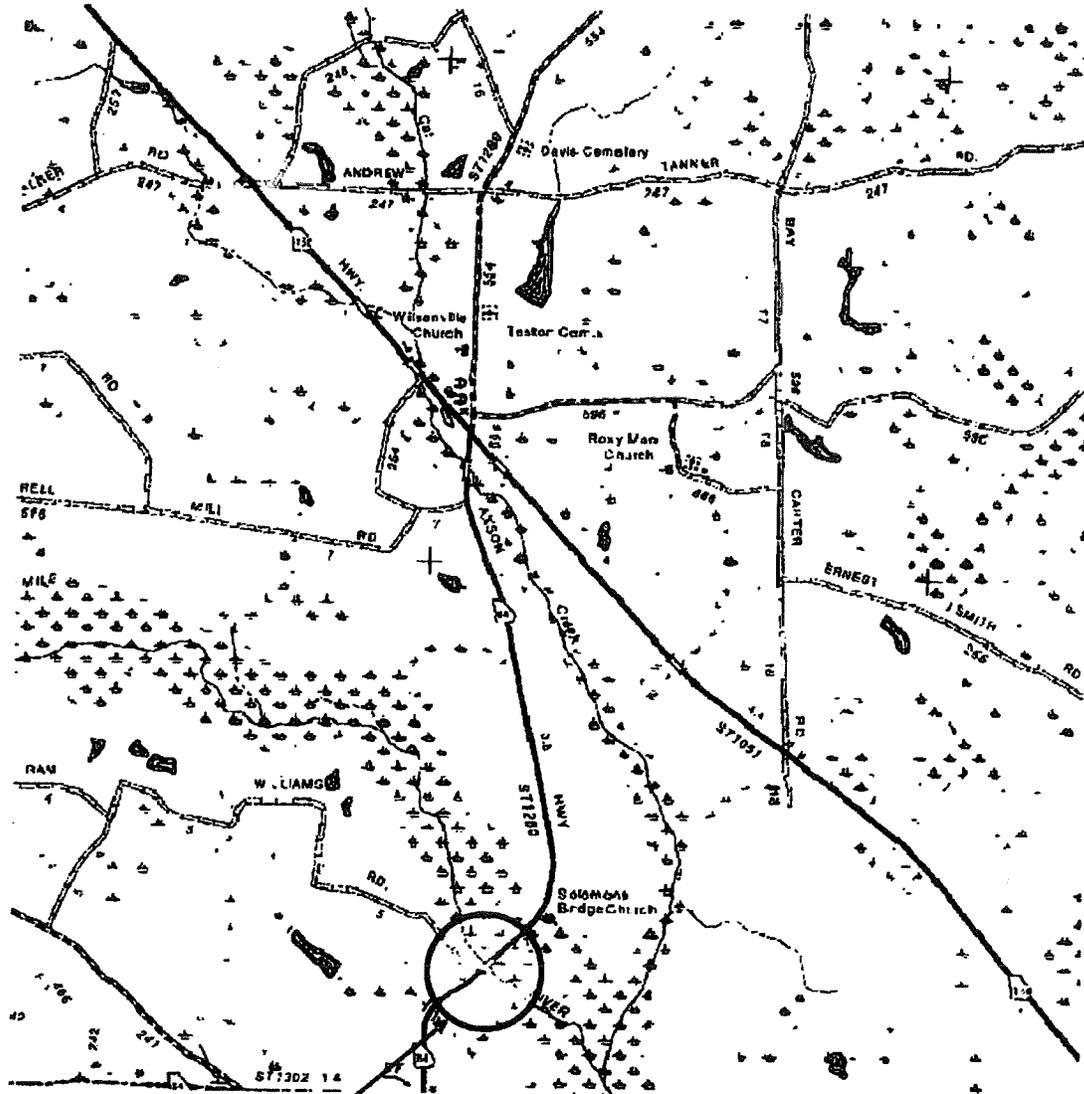

PROJECT LOCATION

# Preconstruction Status Report

## SR 64 @ 17 MILE RIVER 12 MI NE OF PEARSON

PI Number: 0007164

COUNTY: Coffee  
 LENGTH (MI): 0.43  
 PROJ NO: CSBRG-0007-00(164)  
 PROJ MGR: Mosley, Brent A.  
 ACHD INITIALS: BWS  
 OFFICE: Program Delivery  
 CONSULTANT: No Consultant, GDOT In-House Design  
 SPONSOR: GDOT

MPO: Not Urban  
 TIP #: 4  
 MODEL YR: 12  
 TYPE WORK: Bridges  
 CONCEPT: BR REPL  
 BOND PROJ: Replacement  
 DESIGN FIRM: GDOT D4 Design Office

BASELINE LET DAT: 11/21/14  
 SCHED LET DATE: 12/2/16  
 LIGHTING TYPE: None

MGMT LET DATE: 11/21/14  
 WHO LETS?: GDOT Let  
 LET WITH:

Print Date 2/6/14  
 Page 1

BASE START	BASE FINISH	TASKS	ACTUAL START	ACTUAL FINISH	%
8/28/07	9/8/11	Concept Development Summary	8/28/07	9/8/11	100
5/20/10	5/20/10	Concept Meeting	5/20/10	5/20/10	100
9/8/11	9/8/11	Management Concept Approval Complete	9/8/11	9/8/11	100
3/9/12	3/9/13	Environmental Summary	3/13/12	3/15/13	53
12/17/08	3/19/09	Database Summary	12/17/08	3/19/09	100
12/17/08	3/19/09	Field Survey Summary	12/17/08	3/19/09	100
7/12/10	7/28/13	Preliminary Roadway Plans	7/11/10	9/10/13	100
3/9/12	8/28/12	Preliminary Bridge Design Summary	8/9/12	3/15/13	100
1/21/14	7/7/14	404 Permit Summary			0
9/8/13	9/8/13	PFPR Inspection	8/20/13	8/20/13	100
9/10/13	11/18/13	RAW Plans Preparation	8/21/13	10/25/13	100
11/19/13	1/17/14	RAW Plans Final Approval	8/28/13		0
10/18/13	10/18/13	L & D Approval			0
2/17/14	2/17/14	RAW Authorization			0
3/6/12	10/22/12	Soil Survey Summary	8/8/12	4/25/13	100
8/29/12	3/21/13	BFI Report Summary	3/20/13		0
10/17/13	4/2/14	Final Construction Plans	8/22/13		60
10/31/13	3/19/14	Final Bridge Plans Preparation	3/29/13		0
5/8/14	5/8/14	PFPR Inspection			0
9/2/14	9/2/14	Submit Final Plans			0
9/22/14	9/22/14	Construction Authorization			0

Briggs: SKG 2/3/14  
 Design: TB, Not on Bl. Sch, PFPR 8-20-13 (Env. Waiver); updated 8-14-13  
 EIS: CE I NotAppd / RecovFY14ROWMHCert By May 2014 | Treadway/Malia3Feb14  
 EMG: BRIDGE REPLACEMENT  
 Engr Services: PFPR distributed without EA  
 LGFA: NOTIFICATION LETTER SENT TO COFFEE 10-18-06.  
 Programming: #1 2-2012/CONFIRMED EXEMPT PER FHWA 9-7-2012/HZ 6-2013/HZ 9-2013/HZ 1-2014  
 ROW: Detailed Cost Estimate being Prepared, to be turned in by Sept. 27, 2013. RAW Plans to SAAG on 9-18-13  
 Utility: Clear 01/14

Phase	Approved	Proposed	Cost	Fund	Status	Date Auth
PE	2008	2008	\$572,389.09	Q24	AUTHORIZED	8/28/07
ROW	2014	2014	\$120,000.00	M240	PRECST	
CST	2015	2015	\$4,145,705.91	M240	PRECST	
UTL	2015	2015	\$8,639.40	M240	PRECST	

COST ESTIMATES		STIP AMOUNTS	
Activity	Cost	Activity	Fund
PE	\$572,389.09	10/4/13	Q24
ROW	\$120,000.00	9/20/13	ROW
CST	\$4,064,417.56	9/20/13	CST
UTL	\$8,470.00	UTL	UTL

**District Comments**  
 BAM - 1-31-14  
 - Environmental behind schedule  
 - CE document submitted to FHWA on 1-24-13  
 - Team Meeting held 1-6-14 and ENV approval not expected until mid April.  
 - A PCR is being prepared with:  
 June 15 2014 ROW Authorization & March 2015 LET

Pre Parcel CT	5	Total Parcel in ROW System:	5	Cond Filled:	0	Acquired By:	DOT	DEEDS CT:	0
Under Review	0	Options Pending:	0	Relocations:	0	Acquisition MGR:	Bradford, Kim		
Released:	0	Condemnations - Pend:	0	Acquired:	0	RAW Cert Date:			

# NOTICE OF LOCATION AND DESIGN APPROVAL

**CSBRG-0007-00(164) – Coffee County**

**P. I. No. 0007164**

Notice is hereby given in compliance with Georgia Code 22-2-109 and 32-3-5 that the Georgia Department of Transportation has approved the Location and Design of this project.

The date of location and design approval is: **February 25, 2014**

This is a bridge replacement project located in Coffee County on SR 64 over 17 Mile River approximately 12 miles NE of Pearson. The gross project length is 1,950 feet (0.369 miles) with 1,380 feet of roadway and 570 feet of bridge construction. The project begins just north of Lavender Road, approximately ½ mile north of the Atkinson / Coffee County Line. The project is located in the 6<sup>th</sup> Land District in Coffee County

This project will replace the narrow and structurally deficient bridge with a new 570 ft long by 34 ft wide (gutter to gutter deck width) bridge which consists of two 11 ft travel lanes with 6 ft shoulders. Traffic will be maintained by a temporary on-site detour bridge and the proposed bridge will be constructed at existing location.

Drawings or maps or plats of the proposed project, as approved, are on file and are available for public inspection at the Georgia Department of Transportation:

H. Keith Carver, Area Engineer  
[hcarver@dot.ga.gov](mailto:hcarver@dot.ga.gov)  
1835 South Peterson Avenue  
Douglas, GA 31535  
(912)389-4737

Any interested party may obtain a copy of the drawings or maps or plats or portions thereof by paying a nominal fee and requesting in writing to:

Genetha Rice-Singleton, State Program Delivery Engineer  
Office of Program Delivery  
Attn: Brent Moseley, Project Manager  
[bmoseley@dot.ga.gov](mailto:bmoseley@dot.ga.gov)  
204 North Highway 301  
Jesup, GA 31546  
(912)530-4391

Any written request or communication in reference to this project or notice SHOULD include the Project and P. I. Numbers as noted at the top of this notice.
