

ORIGINAL TO GENERAL FILES

**DEPARTMENT OF TRANSPORTATION  
STATE OF GEORGIA**


---

**OFFICE OF DESIGN POLICY & SUPPORT  
INTERDEPARTMENTAL CORRESPONDENCE**

**FILE** P.I. #0009865  
GDOT District 4 - Tifton  
Lee County  
SR 118 @ Muckaloochee Creek

**OFFICE** Design Policy & Support

**DATE** December 10, 2013

**FROM**  for Brent Story, State Design Policy Engineer

**TO** SEE DISTRIBUTION

**SUBJECT** APPROVED LOCATION & DESIGN REPORT

Attached is the approved Location and Design Report with Notice of Location & Design Approval for the above subject project.

Attachment

DISTRIBUTION:

Bobby Hilliard, Program Control Administrator  
Genetha Rice-Singleton, State Program Delivery Engineer  
Glenn Bowman, State Environmental Administrator  
Ben Rabun, State Bridge Engineer  
Kathy Zahul, State Traffic Engineer  
Phil Copeland, State Right-of-Way Administrator  
Lisa Myers, State Project Review Engineer  
Andy Casey, State Roadway Design Engineer  
Attn: Clay Bastian  
Cindy VanDyke, State Transportation Planning Administrator  
Jeff Fletcher, Location Bureau Chief  
Angela Robinson, Financial Management Administrator  
Joe Sheffield, District Engineer  
Brent Thomas, District Preconstruction Engineer  
Shane Pridgen, District Planning & Programming Engineer  
William Cooper, Area Engineer - D4, A5  
Brent Mosley, Project Manager  
BOARD MEMBER - 2nd Congressional District





## NOTICE OF LOCATION AND DESIGN APPROVAL

**Project No.: N/A, Lee County**

**P.I. No. 0009865**

Notice is hereby given in compliance with Georgia Code 22-2-109 and 32-3-5 that the Georgia Department of Transportation has approved the Location and Design of this project.

The date of location and design approval is: Dec 10, 2013

This project, P.I. No. 0009865, is a bridge replacement project located in Lee County on SR 118 over the Muckaloochee Creek just east of Smithville. The gross project length is 900 feet (0.171 miles) with 735 feet of roadway and 165 feet of bridge construction. The project will begin on SR 118 just east of Robertson Street and end at the Smithville City Limits. The project will replace the existing structurally deficient 111 ft long by 30 ft wide bridge and existing 11.5 ft travel lanes with 2 feet shoulders with a new 165 ft long by 40 ft wide (gutter to gutter deck width) bridge and two 12 ft travel lanes with 8 ft shoulders. The project will construct the new bridge in existing location while providing an off-site detour. The project is located in the 16<sup>th</sup> Land District in Lee County.

This project will replace the substandard bridge over Muckaloochee Creek on SR 118. The project will construct the new bridge in existing location while providing an off-site detour.

Drawings or maps or plats of the proposed project, as approved, are on file and are available for public inspection at the Georgia Department of Transportation:


William H. Cooper, Area Engineer  
[wcooper@dot.ga.gov](mailto:wcooper@dot.ga.gov)  
2060 Newton Road  
Albany, GA 31701  
(229)430-4198

Any interested party may obtain a copy of the drawings or maps or plats or portions thereof by paying a nominal fee and requesting in writing to:

Genetha Rice-Singleton, State Program Delivery Engineer  
Office of Program Delivery  
Attn: Brent Moseley, Project Manager  
[bmoseley@dot.ga.gov](mailto:bmoseley@dot.ga.gov)  
204 North Highway 301  
Jesup, GA 31546  
(912)427-5749

Any written request or communication in reference to this project or notice SHOULD include the Project and P. I. Numbers as noted at the top of this notice.

Project Concept Report page 2  
Project Number: 0009865-CST  
P. I. Number: 0009865  
County: Lee

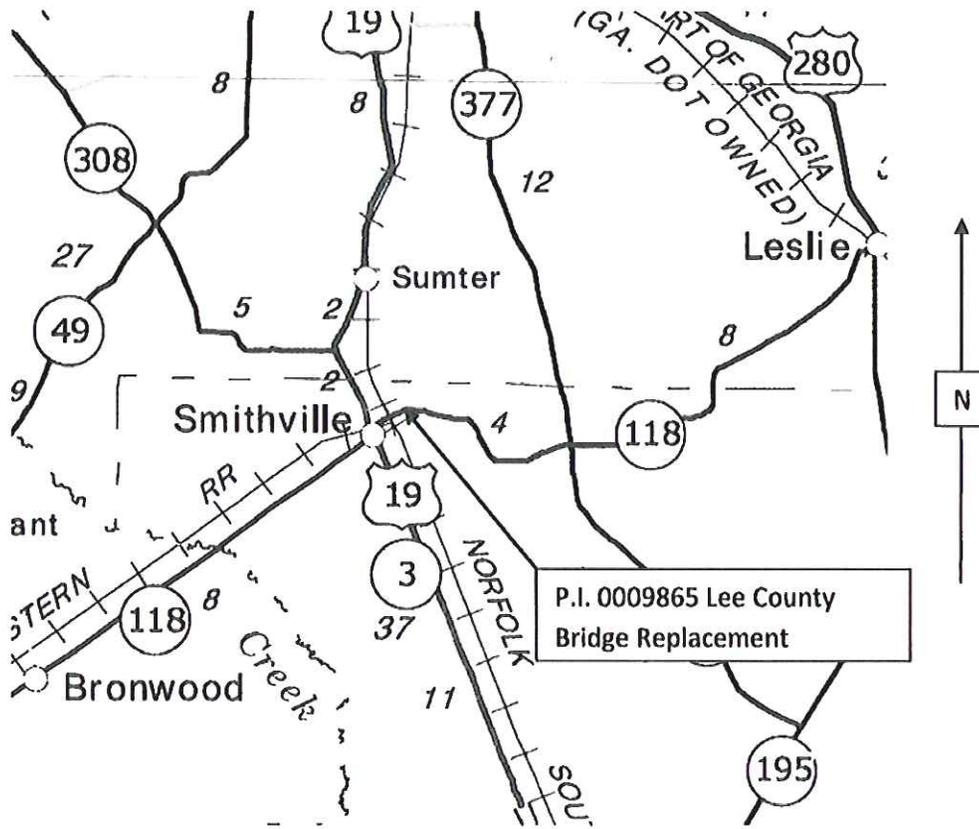

Location Sketch

Preconstruction Status Report

**PI Number:** 0009865  
**COUNTY:** Lee  
**LENGTH (M):** 0.1  
**PROJ NO:** Mesley, Brent A.  
**ACHD INITIALS:** BWS  
**OFFICE:** Program Delivery  
**CONSULTANT:** No Consultant, GOOT In-House Design  
**SPONSOR:** GOOT

**SR 118 @ MUCKALOOCHEE CREEK**  
**IMPO:** Not Urban  
**TIP #:**  
**MODEL YR:**  
**TYPE WORK:** Bridges  
**CONCEPT:** BR REPL  
**PROG TYPE:** Replacement  
**BOND PROJ:** GOOT Roadway Design C  
**DESIGN FIRM:** Bascon

**PRIORITY CD:** 4  
**DOT DIST:** 2  
**CONG. DIST:** N  
**BIKE:** N  
**MEASURE:** E  
**SUFF:** 69.75

**BASELINE LET DATE:** 2/4/15  
**SCHED LET DATE:** 7/7/16  
**LIGHTING TYPE:** None  
**NGMT LET DATE:** 2/4/15  
**NGMT ROW DATE:** 8/15/13  
**WHO LETS?** GOOT Ltr  
**LET WITH:**

**Print Date:** 11/18/13  
**Page:** 1

Phase	Approved	Proposed	Cost	Fund	Status	Date Auth
PE	2011	2011	\$250,000.00	Q10	AUTHORIZED	1/12/11
ROW	2014	2014	\$120,000.00	M232	PRECST	
CST	2015	2015	\$1,148,770.91	M232	PRECST	

Phase	Approved	Proposed	Cost	Fund	Status	Date Auth	STIP AMOUNTS			
							Activity	Cost	Fund	
PE	2011	2011	\$250,000.00	Q10	AUTHORIZED	1/12/11	4/15/10			
ROW	2014	2014	\$120,000.00	M232	PRECST		9/20/13	PE	\$50,000.00	Q10
CST	2015	2015	\$1,127,226.39	M232	PRECST		8/12/13	ROW	\$105,090.40	M232
								CST	\$978,261.09	M232

ACTUAL START	ACTUAL FINISH	%	TASKS
3/1/11	3/6/14	100	Concept Development Summary
9/22/11	9/22/11	100	Concept Meeting
11/28/11	11/28/11	100	Management Concept Approval Complete
3/2/11	0	0	Public Information Open House Held
4/15/11	7/20/11	100	Environmental Summary
4/15/11	7/20/11	100	Database Summary
1/17/11	11/15/12	100	Field Survey Summary
6/27/12	10/28/12	100	Preliminary Roadway Plans
2/14/13	2/14/13	100	Preliminary Bridge Design Summary
3/18/13	5/7/13	100	404 Permit Summary
7/17/13	0	0	FPFR Inspection
4/11/11	3/12/12	100	R/W Plans Preparation
10/26/12	61	61	R/W Plans Final Approval
2/12/13	70	70	L & D Approval
	0	0	RAW Authorization
	0	0	Soil Survey Summary
	0	0	BFI Report Summary
	0	0	Final Construction Plans
	0	0	Final Bridge Plans Preparation
	0	0	FPFR Inspection
	0	0	Submit Final Plans
	0	0	Construction Authorization

**Bridge:** SWW 11/4/13  
**Design:** CCB, need ENV to complete R/W, following PM's recovery sched. 10/31/13  
**EIS:** CEID6Nov13(RecovFY13RWWillCenByApr14ISams07Nov13  
**ENG:** NOT APPLICABLE  
**Engr Services:** FPFR Report distributed without EA.  
**LGPA:** NOTIFICATION LETTER SENT TO LEE & SMITHVILLE 11-19-10.  
**PDD:** Reviewed 6/25/2010. Need baseline schedule for CST in FY2017.  
**Programming:** #1 4-2011(CONFIRMED EXEMPT PER FHWA 6-7-2012  
**ROW:** Need ROW Plans & Funding  
**Traffic Op:** IPFRsent1/31/13 W/R  
**Utility:** CLEAR 03/13

**District Comments:**  
 BAM - 10-17-13  
 - Environmental Document not expected until beginning of March due to Ecology. Ecology approved on 10-1-13.  
 - Will not meet ROW Authorization date  
 - Recovery Plan has been submitted proposing an April 2014 ROW Authorization.

Pre Parcel CT	5	Total Parcel in ROW System:	Cond Filed:	Acquired by:	DOT	DEEDS CT:
Under Review		Options Pending:	Relocations:	Acquisition MGR:	Stewart, Chris	
Released:		Condemnations - Pend:	Acquired:	ROW Cert Date:		
